

ROAD AND UTILITY BOND PROJECT INFORMATION

Bankhead Hwy.

Design Start Date: 10/1/2018

Construction End Date: 4/27/2020

Project Type: PAVING

Project Limits: Front Street to Midkiff Rd.

Project Phase: Completed

Next Activity: Project Complete

Project Scope: To install new water lines within

the street right-of-way. To construct improvements of new pavement, curb and gutter

and ADA ramps.

Point of Contact: Matt Carr, P.E. Vicin

432-685-7287

mcarr@midlandtexas.gov

Design: In-house Project

432-685-7287 Engineering Services

City of Midland

Contractor: Salinas Construction Tech

3734 FM 3006

Pleasanton, Texas 78064

Comments: Project completed on time and


on budget.

Authorized Funding Amount: \$1,419,108.02 **Construction Cost:** \$1,369,766.78

Project Photo:



Vicinity Map:

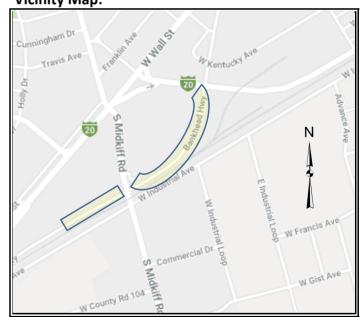

Time

Utility Schedule:

2019' 2020'

JAN FEB MAR APR MAYJUN JUL AUG SEP OCT NOV DEC JAN FEB MAR APR MAYJUN JUL AUG SEP OCT NOV DEC JAN

Paving Schedule:

2019' 2020' 2021' JAN FEB MAR APR MAYJUN JUL AUG SEP OCT NOV DEC JAN FEB MAR APR MAYJUN JUL AUG SEP OCT NOV DEC JAN

AN FEB WAR APR WATJON JOL AUG SEP OCT NOV DECJAN FEB WAR APR WATJON JOL AUG SEP OCT NOV DEC JAN

Legend - Survey Plan Design Delay Bid Construction
